
# Capital Improvement Program Project Update


City of Upland Public Work Committee Meeting January 9, 2024



#### FY 2023-2024 CIPs



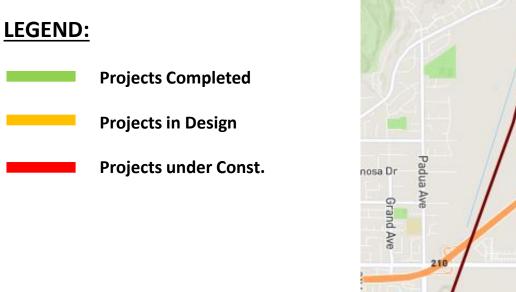

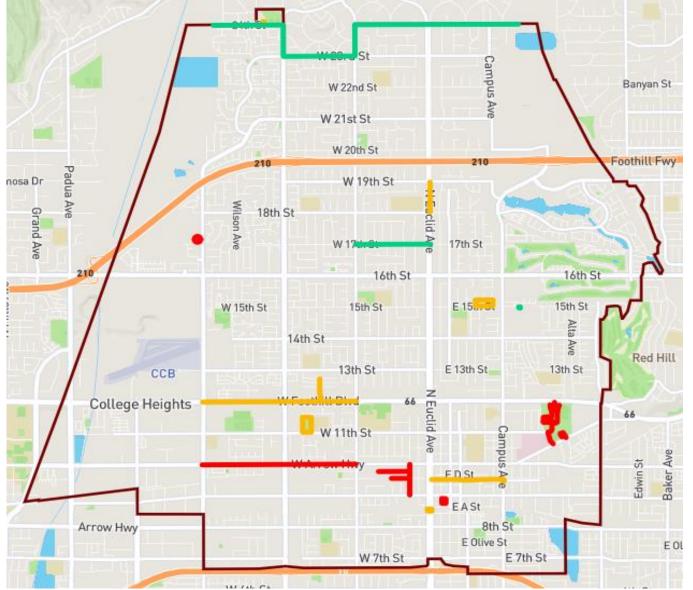

### **Projects in Design**



- Citywide Slurry Seal Annual Program (95% complete)
  - Working with Caltrans for the State permit for a portion of the project on Campus Avenue under the 210 Freeway.
- Baldy View Dog Park Improvements (95% complete)
  - Architect preparing Special Provisions and finalizing the structural specifications.
  - Anticipate bidding late Jan. / early Feb.
- Downtown Public Parking Imp. S. side 'A' St. (75% complete)

### Projects in Design (cont.)

- Foothill Blvd. Benson to Mountain (35% complete)
  - New water main, paving, and ADA improvements
- Foothill Blvd. Mountain to San Antonio (35% complete)
  - New water main, paving, and ADA improvements
- Mulberry Ave. Rehab Foothill to Pine St. (95% complete)
  - > New water main, paving, and ADA improvements.



## Projects in Design (cont.)

- -te
- Ph. II of the Metrolink Sta. Accessibility Proj. (100% Complete)
  - County is Lead Agency. SBCTA Board expected to award a construction contract in Jan 2024.
- Water Facility Back-Up Power Generators at Plant 2 on 24<sup>th</sup> St. and Plant 6 on 15<sup>th</sup> St. (98% complete)
  - Final plans under review
  - Anticipate bidding late Jan. / early Feb.

#### **Projects under Construction**

- 17<sup>th</sup> St. Rehab. San Antonio to Euclid (complete)
  - \$2.66 million final construction cost.
  - $\blacktriangleright$  Work accepted by City Council on 1/8/2024.
- Alpine / Vernon / Palm Ave. Rehab. (7% complete)
  - ▶ \$4.3 million construction contract.
  - Working on new water main on Palm Avenue.
- Memorial Park Parking Lot Improvements (contract awarded)
  - $\blacktriangleright$  \$1.15 million contract awarded on 12/11/2023 to Onyx Paving Company.
  - $\blacktriangleright \quad \text{Preconstruction meeting scheduled for } 1/16/2024.$



### Projects under Construction (cont.)

- Parking Lot Rehab 1<sup>st</sup> Ave. & 'A' Street (21% complete)
  - \$1.3 million contract awarded to Gentry General Engineering.
  - Working on new water main in the south alley.
- Pavement Management System Update (62% complete)
  - Citywide system PCI survey and evaluation.
  - Street, alley, and parking lot scanning by Transmap is complete and the raw data is being processed.



### Projects under Construction (cont.)

- CALL OF UP
- Reservoir 2 & 16 Air Gaps Installation (contract awarded)
  - \$121,000 contract awarded on 11/13/23 to T.E. Roberts, Inc.
  - Staff is reviewing contractor submittal items.
  - Preconstruction meeting tentatively scheduled for next week.
- Reservoir 15 Replacement at 17<sup>th</sup> St. (99% complete)
  - Completing SCADA integration, system operational testing, and staff training.
- Arrow Hwy. Rehab Benson to San Antonio (9% complete)
  - > \$9.8 million construction contract awarded to All American Asphalt.


#### Arrow Hwy – Benson to San Antonio





## Arrow Highway Project Update


- Original Const. Schedule: Nov 2023 Oct 2024 (300 Cal. Days)
- Improvements completed to date:
  - ✓ 127 LF of CML&C water main installed
  - ✓ 6 water valves installed
  - 27 water service laterals installed
  - ✓ 11 fire hydrants upgraded
  - ✓ 4,248 SF of sidewalk replaced
  - ✓ 66 SF of driveway approaches replaced

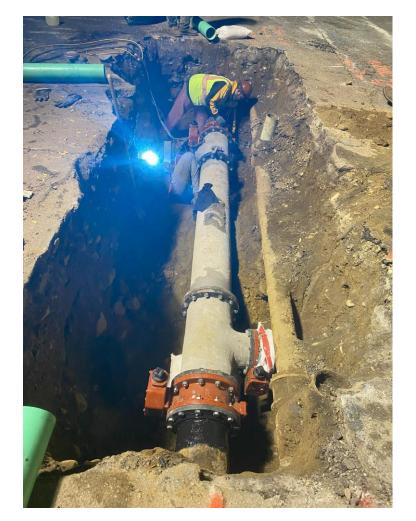




## Arrow Highway Project Update (cont.)

- Major near-term improvements 1/22/24 thru 1/26/24:
  - Partial intersection shut-down at Benson Avenue & Arrow Hwy. for the WFA 42" water main shut-down, dewatering, and relocation.

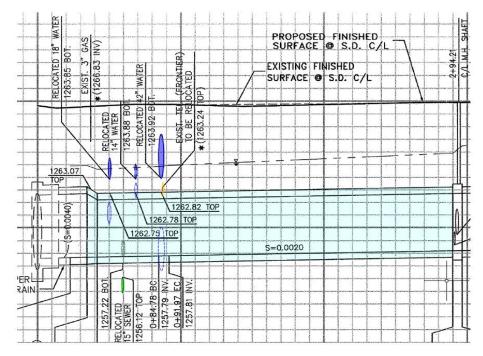

Arrow Hwy. Profile View

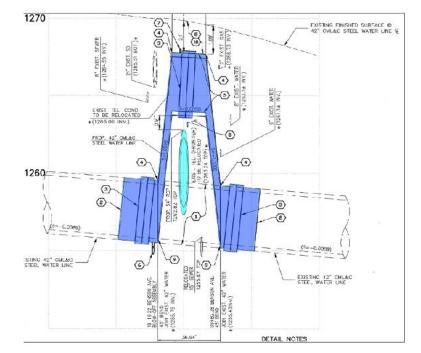



Benson Ave. Profile View


## Arrow Highway Project Update (cont.)

• Major future improvements at Benson & Arrow intersection:



- MWD 18" water main shut-down, dewatering, and relocation.
- City 14" water main shut-down, dewatering, and relocation.
- Frontier fiber optic conduit relocation and/or protect in place, depending upon excavated condition.
- City 15" sewer main relocation (lowering) for 600 LF along Benson Ave.

#### Arrow Highway Project Update (cont.)

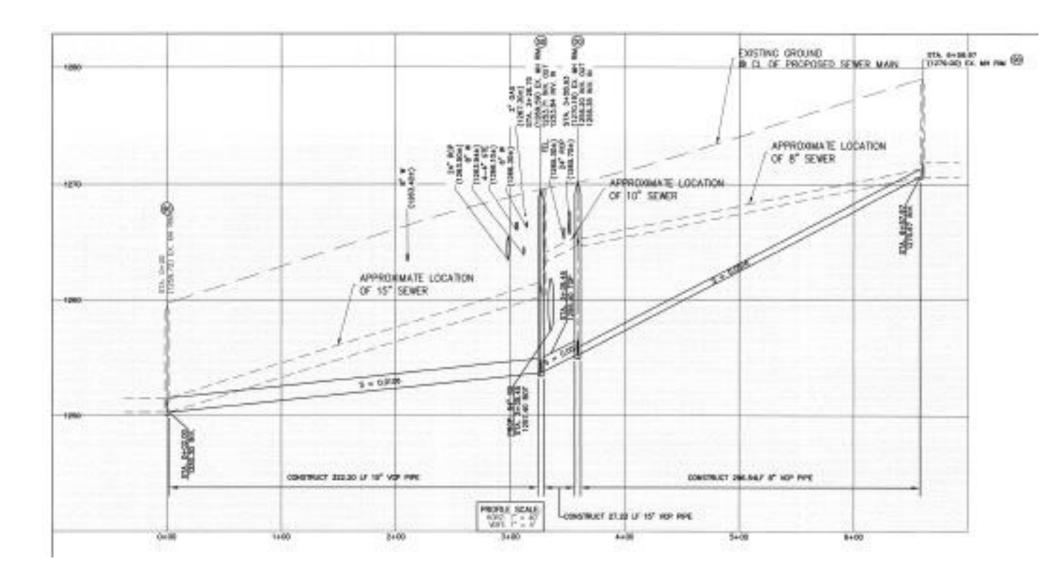





#### It is staff's recommendation that the Public Works Committee Receive and File the Presentation.
